




Housing Authority
Surprise Safety Inspection Programme (SSIP)
Good & Bad Practices
香港房屋委員會
突擊安全巡查計劃
Q2 & Q3 2018 良好及不良作業



職業安全健康局
OCCUPATIONAL SAFETY & HEALTH COUNCIL

得分一覽

SSIP Median Scores at a Glance

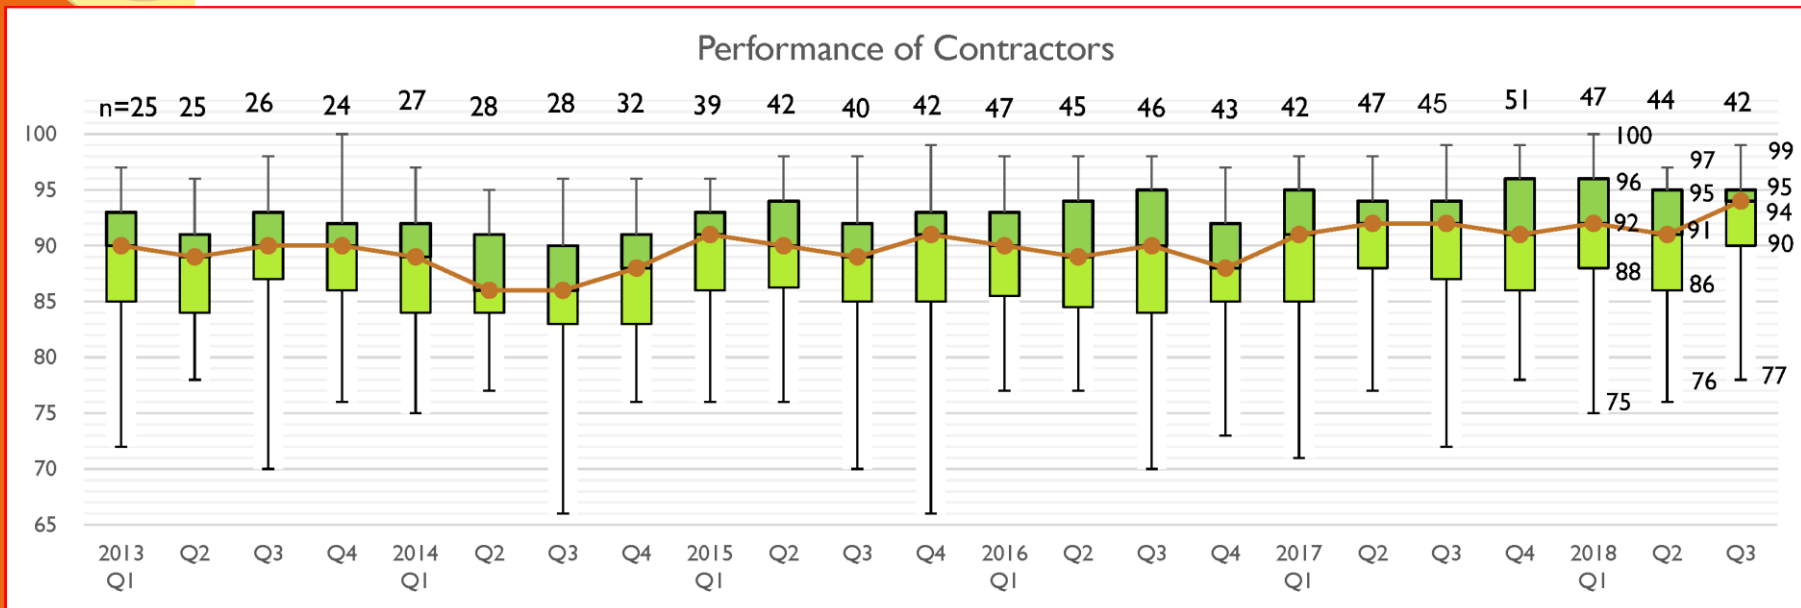



Summary of Good Practices

良好作業摘要

- Good practices were observed in fist grip wire clips were found at main wire of gondola; clear warning notice for floor openings; using picture to indicate the purpose of container and provision of name tags for switch in distribution board.
- 良好作業包括：於吊船主纜末端使用合適威也夾；孔洞提供明確警告告示；以圖片表示收集容器用途；於電箱內掣位加設名牌。


於吊船主纜末端使用合適威也夾。

Fist grip wire clips were used at main wire of gondola.



孔洞提供明确警示。

Clear warning notice for the floor opening.

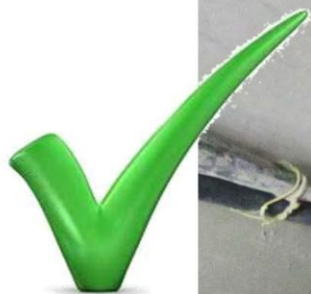

以圖片表示收集容器用途。

Photo was used to indicate the purpose of container.



於電箱內掣位加設名牌。

Name tags were installed for identifying switches in distribution board.



電線妥善掛高。

Electric cables were properly hung.





END
完

現在放映的是

2018年11月7日

香港房屋委員會

「新工程合約工地安全講座」的片段

台上的講者是

職業安全健康局高級顧問 張名銑先生

他的講題是突擊安全巡查計畫 - 2018年第2季及第3季巡查結果

現在我講解過去兩季突擊安全巡查 (SSIP) 在房委會工地

所看到的良好作業

我們直至今年執行了五年有多

SSIP 中位數亦有輕微上升

那麼良好的作業例如

吊船主纜上使用了合適的威也夾

根據作業守則 (COP) 這一款是合規格的

亦發覺有人使用

這是一些地洞

最近亦較多人關注

我們亦有特別去查看

亦有一些良好例子

如地洞上會有警告標示

亦牢固地掩蓋好地洞

這個就較為特別

這個亦是五常法 (5S) 的做法

在收集器外

以圖片表示裝了什麼垃圾

希望圖片的展示是真確的

於電箱內的標籤

很少會看到寫得這麼仔細

電線妥善高掛

好 講解到此

謝謝大家
多謝觀看
