Housing Authority Surprise Safety Inspection Programme (SSIP) Good & Bad Practices 香港房屋委員會 突擊安全巡查計劃 Q4 2019 & Q1 2020 良好及不良作業




2020 Q1

1

2





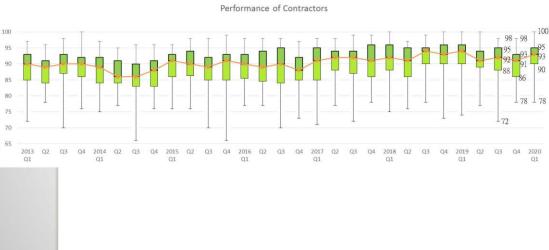

2020 Q1



## Summary of Good Practices 良好作業摘要

- Good practices were observed in the provision of proper access equipment; provision of sufficient material skips for material storage; display of real time working load for tower crane; and provision of charging station for cordless hand-held tools.
- 良好作業:提供合 適工作通道;提供 足夠物料斗儲放物 料;為天秤提供實 時負重操作資料; 及在地盤提供充電 站為無線電手工具 充電。

2020 Q1



提供合適工作通道。 Provision of proper access equipment.



2019 Q

## 提供足夠物料斗儲放物料。

Provision of sufficient material skips for material storage.



2020 Q1

<image><section-header>

2019 Q

5

## 在地盤提供充電站為無線電手工具充電。

Provision of charging station for cordless hand-held tools.



2020 Q1

 $\mathcal{I}$ 

7



8

## Title: Site Safety Seminar for Capital Works New Works Contracts

Super	Site Safety Seminar for Capital Works New Works Contracts 16 July 2020
VO:	Here is the footage from Site Safety Seminar for Capital Works New Works Contracts which was held on 16 July 2020
Super	Senior Consultant of Occupational Safety and Health Council Mr. Henry CHEUNG His presentation topic is "Surprise Safety Inspection Programme (SSIP) – Findings in Quarter 4 of 2019 & Quarter 1 of 2020"
VO:	The speaker is Mr. Henry CHEUNG Senior Consultant of Occupational Safety and Health Council His presentation topic is Surprise Safety Inspection Programme (SSIP) Findings in Quarter 4 of 2019 & Quarter 1 of 2020
Mr. Cheung:	Hello, everyone! I would share the findings of the surprise safe inspections in Q4 of 2019 and Q1 of 2020 We should give recognition to the good practices and also learn from the bad practices It is 2020 this year The median score for Q4 2019 was 91 points It was 93 points for Q1 2020 Let us look at some positive examples first For this working floor planks were laid to allow safe access This was commendable There were mid and top guard-rails with good planks These were quite uncommon, so this was really commendable Material skips were neatly organised without materials being too high or overflowing For organised waste dumping, material skips would not overflow This was a relatively new way of working The tower crane gave immediate, real-time feedback on the spot using the traffic light colour system to show if the weight had exceeded safety guidelines It was very easy to understand For new contracts, cordless portable electric tools were used They were charged at a spot sheltered from wind and rain This was a good example

That is all for my sharing today Thank you

VO: Thank You For Watching
