

Housing Authority Surprise Safety Inspection Programme (SSIP) Good & Bad Practices for 2025 Q2 & Q3

香港房屋委員會
突擊安全巡查計劃
2025 Q2 & Q3 良好及不良作業






職業安全健康局
OCCUPATIONAL SAFETY & HEALTH COUNCIL



得分一覽

SSIP Median Scores at a Glance

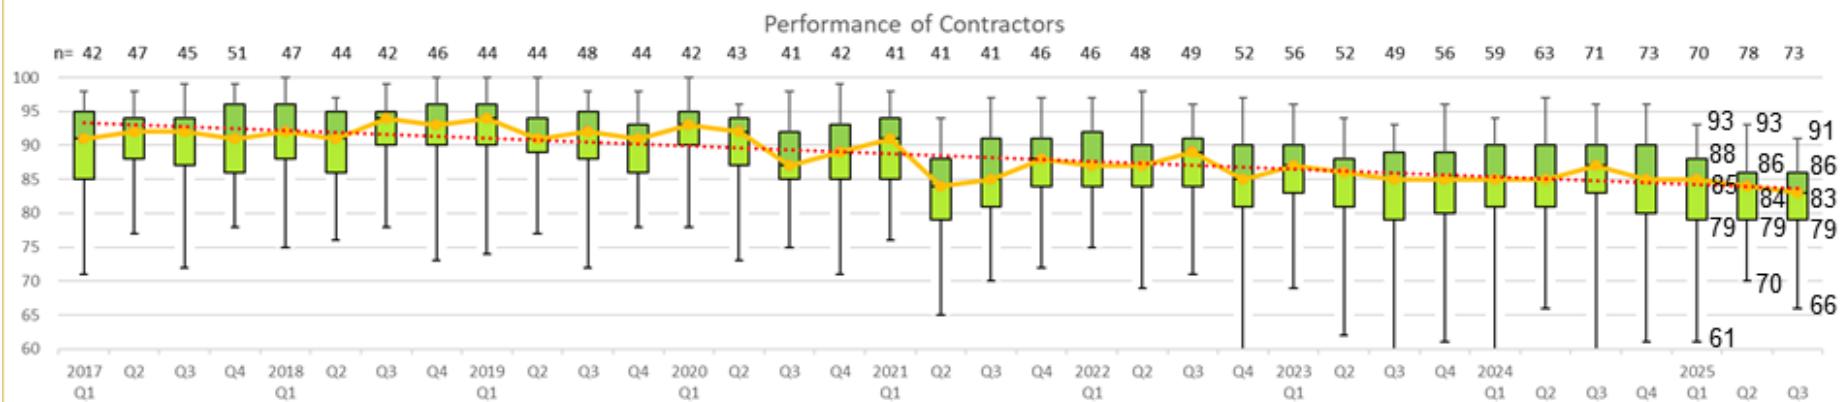



Summary of Good Practices

良好作業摘要

- Good practices were observed including additional guard-rails for fall protection; visualized construction procedures; clear demarcation of pedestrians and vehicles; provision of CMP for real time monitoring; proper arrangement of rest periods for workers; provision of heat stroke prevention equipment, provision of tool strap with appropriate internation/national standards, etc.
- 良好作業包括：加高防護欄杆以防止人體從高處下墮；圖象化的施工程序；清晰的人車分隔；提供綜合管理平臺對工地進行即時監控等；工人休息時間的適當安排；提供防中暑設備；提供符合國際/國家標準的工具手繩。

GOOD PRACTICE 良好作業方式



在矮牆安裝額外的防護欄杆以防止下墮。

Provision of additional guard-rails for fall protection at the parapet wall.



清晰的人車分路設施。

Clear demarcation of pedestrians and vehicles was seen on site.




GOOD PRACTICE 良好作業方式



提供CMP（綜合管理平臺）對工地進行即時監控。

Provision of CMP for real time monitoring.

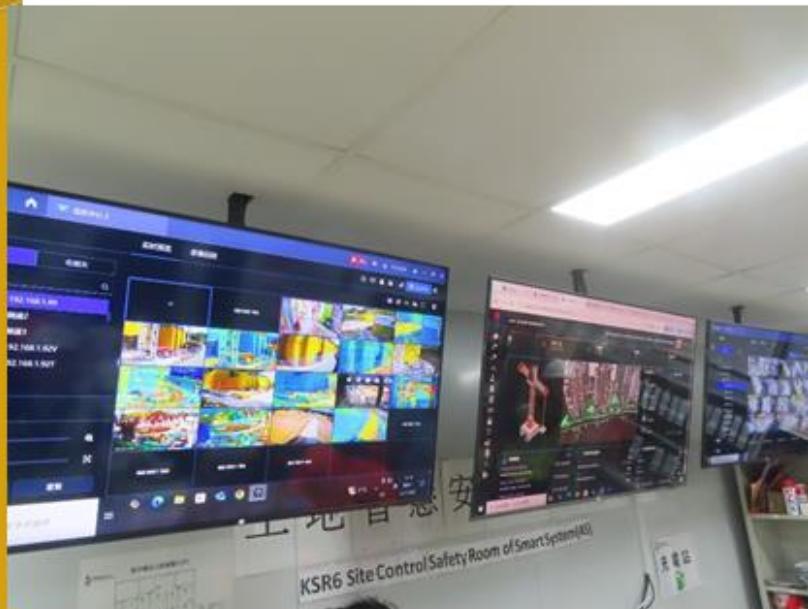

在酷熱天氣下工作，將工友分成不同組別休息。

Workers were divided into assigned groups to take breaks during working in hot weather.



GOOD PRACTICE 良好作業方式



提供符合國際/國家標準的工具手繩，例如ANSI/ISEA 121-2018。

A tool strap with appropriate international/national standards such as ANSI/ISEA 121-2018 was provided.



GOOD PRACTICE 良好作業方式




在工作位置提供大型風扇。
Provision of large fans at working location.



良好計劃工地內的機械分佈及運輸路線，並圖象化顯示於當眼位置。此外，安排指定管理人員管理不同的分區，並張其負責範圍顯示在計劃內。

A visualized planning for machinery distribution and transport routes at prominent location on the construction site .
Additionally, assign designated personnel to manage different zones and incorporate this information into the plan.





END
完
